

---

Project Update – OC Mtg. 6-20-12

# STATEWIDE RADIO NETWORK



# Statewide Radio Network Project Update

## Engineering design and procurement

- VELCO internal and external Automatic Vehicle Location (AVL) mapping tool continues testing and is visible to external users.
- Engineering and design continues for remaining four sites.

## Field work

- 24 radio sites commissioned and acceptance tested
- Seven sites in construction phase.
- Coverage field testing meeting expectations.
- All core radio controllers are in-service.
- Final commissioning and acceptance testing in-progress.




# Statewide Radio Network Project Update

## Regulatory activities

- CPG approval received for 30 SRP transmit sites
- CPG application submitted and pending for Sharon site
- Wells radio site condemnation
  - PSB Proposal For Decision released in May
  - Hearing officer ruled in VELCO's favor on all vital elements
  - Value set at \$25,750
  - Anticipate landowners to appeal valuation to Vt Supreme Court
  - Preparing for site construction

## Schedule

- Ready for traffic July 2012.
- User cutovers to begin Q3 2012.

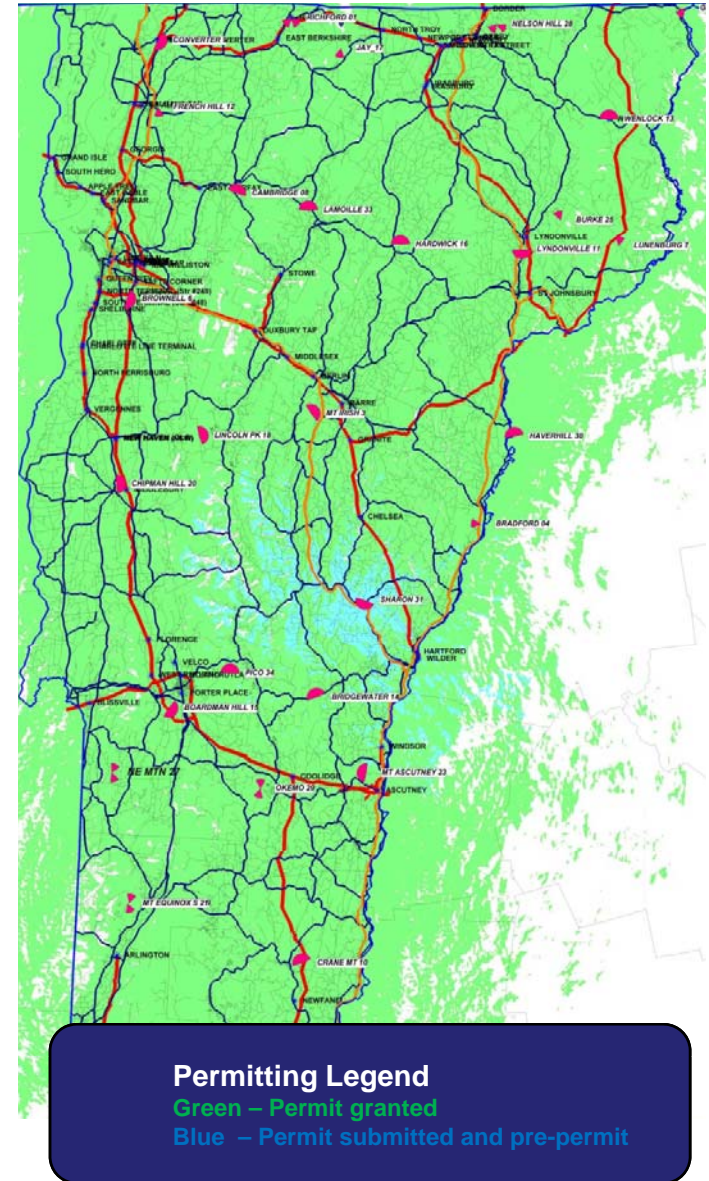

# Statewide Radio Network Project Update

## Site Activities:

- VEC providing backhaul at 4 sites
  - Richford, Cambridge, Wenlock, Jay
- CVPS providing backhaul at 4 sites
  - Pico, Crane, Equinox North, Equinox South
- GMP co-location at Searsburg
- Integration meetings continued in May

