

Project Update – OC Mtg. 7-19-12

STATEWIDE RADIO NETWORK



Statewide Radio Network Project Update

Engineering design and procurement

- Network coverage is meeting expectations
- VELCO internal and external Automatic Vehicle Location (AVL) mapping tool is operational and is available for external users to view
- Engineering and design continues for remaining two sites of 35

Field work

- 26 sites are commissioned
- Five sites in construction phase
- Two in permitting
- All core radio controllers are in-service
- Test radios are available to DU's where coverage exists




Statewide Radio Network Project Update

Regulatory activities

- CPG approval received for 31 sites
- Wells radio site condemnation
 - PSB Final Decision pending
 - Anticipate landowners to appeal valuation to Vt Supreme Court
- Gearing up for final two sites to enter permitting phase

Schedule

- Ready for traffic Oct 2012
- User cutovers could begin 4Q2012

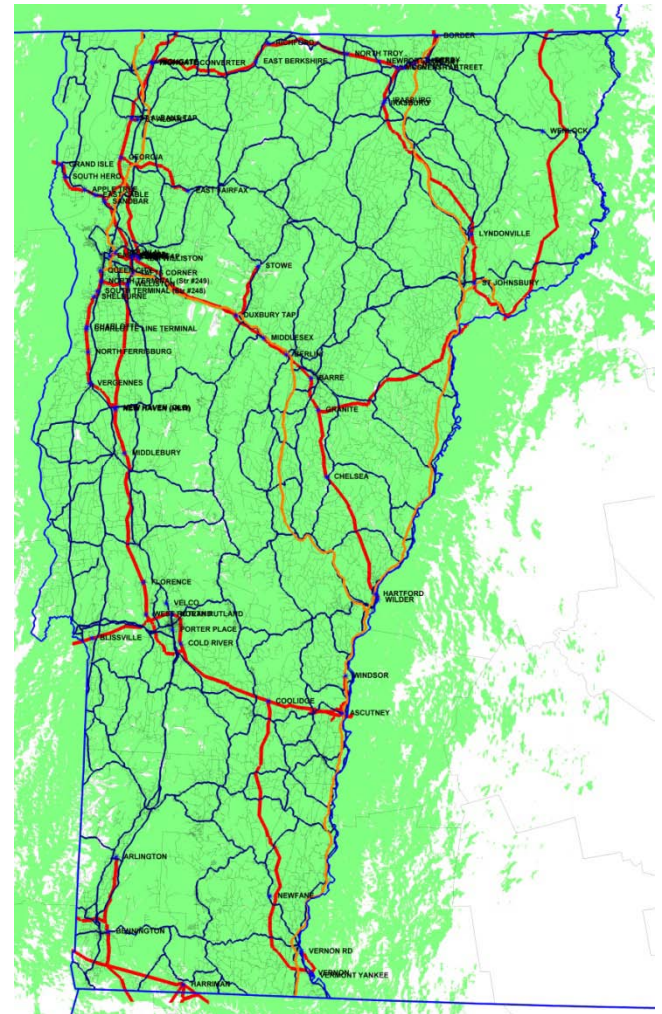

Permitting Legend

Green – Permit granted

Blue – Permit submitted and pre-permit

